



## NATIONAL ASSOCIATION OF POSTAL SUPERVISORS

*National Headquarters*  
1727 KING STREET, SUITE 400  
ALEXANDRIA, VA 22314-2753  
(703) 836-9660

May 5, 2023

### **Board Memo 034-2023: RPDC Update**

#### **Executive Board,**

Attached is the RPDC update as of May 4, 2023. Please take note of the following updates.

- The Richmond and Atlanta RP&DC will be the first to come on line
- USPS states that Local NAPS is being engaged as appropriate
- Questions on proposed staffing (floor plans are 100% completed) must be continually made at all levels as opportunities arise
- Questions on impacts on P&DC, PDF, ISC and NDC's must continually be made at all levels as opportunities arise

If you have questions or concerns, please submit them to me for addressing during the bi-weekly meeting on RP&DC deployment.

Please share this information with your membership.

Thank you and be safe.

NAPS Headquarters

# Union RPDC Updates

Engineering

Processing

Logistics

5/4/2023

# **Richmond Regional Processing & Distribution Center (RPDC)**

**Engineering Design**

**Logistics Design**

**Processing & Maintenance Transition,  
Implementation, & Complement**


# PPM/Engineering US-R-0002 Richmond VA

This region covers a portion of Richmond and Norfolk, Virginia Metro Areas handling the following 3-digit ZIP codes:

233, 234, 235, 236, 237, 279, 224, 225, 229, 230, 231, 232, 238, 239, 244

The Regional Processing and Distribution Center in Richmond is slated for a minor rehabilitation and workroom reorganization

Two Local Processing Centers are associated in the region. The RPDC Region is centered in Sandston, VA. US-R-0001

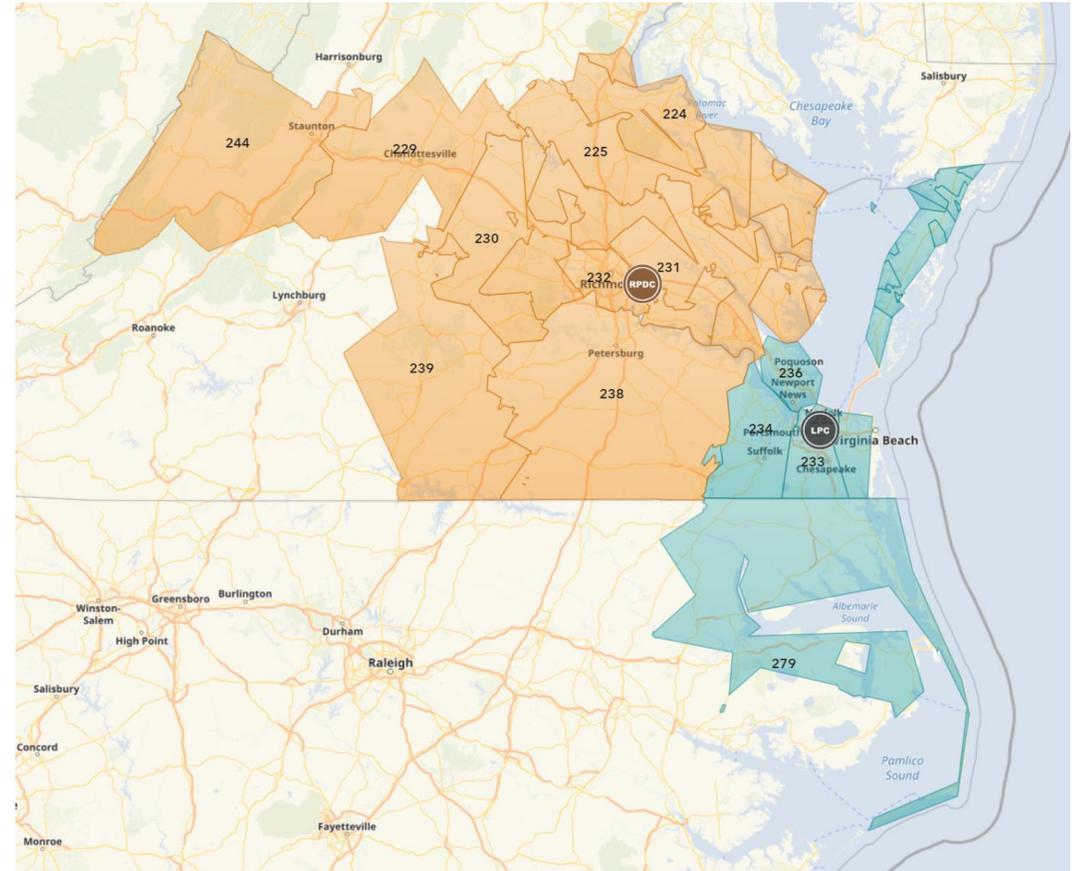


# Richmond - Construction

Ball decking Ram Lifts and Scales have been installed.



Ball decking panel installation ongoing.

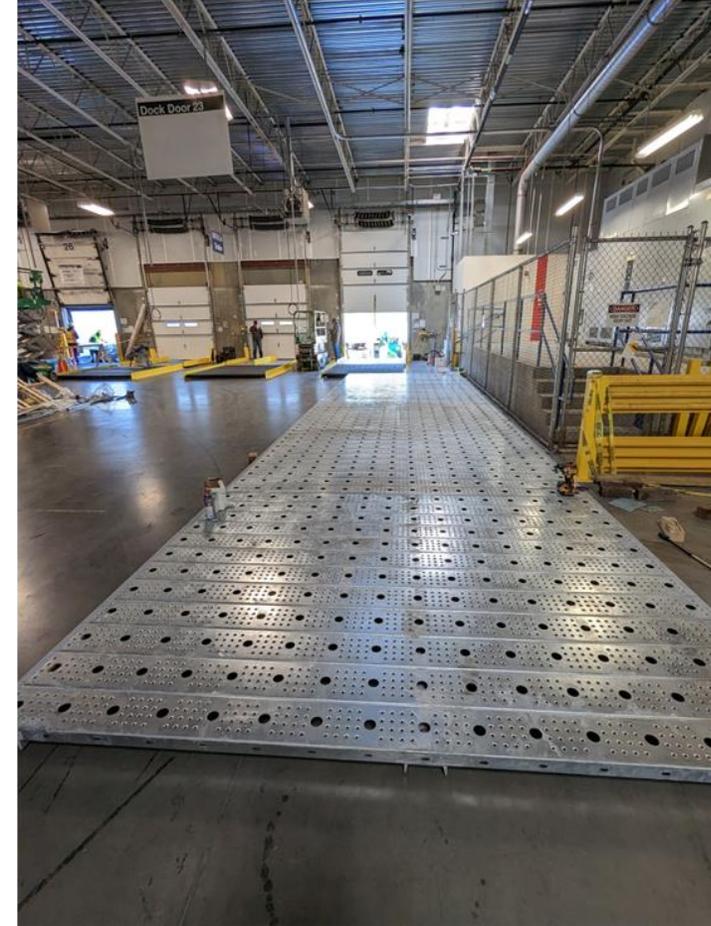


# Richmond - Construction

DBCS moves and power connections successfully completed.



HOPS #2 electrical work near completion.

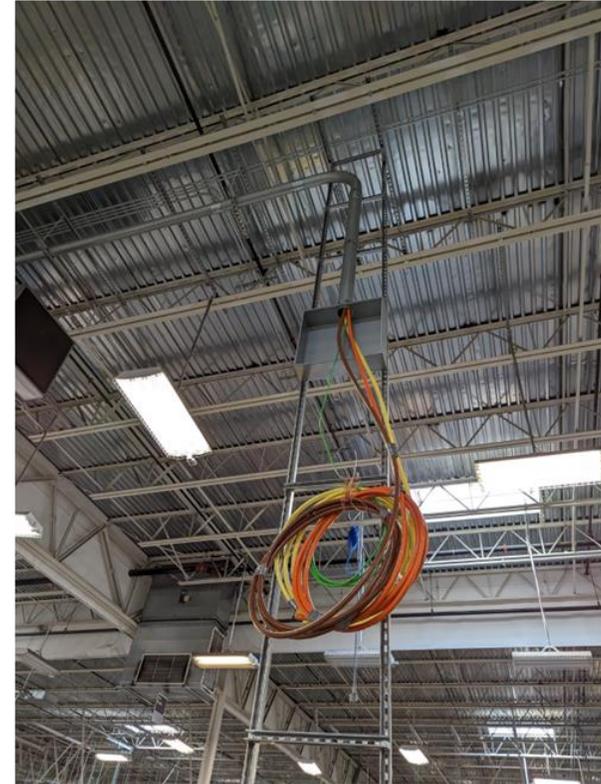

# Richmond – New equipment and systems


## HOPS Installation




- HOPS #1 Mechanical Installation 95% Complete.
- Wiring is underway.

# Richmond - New equipment and systems

## Overhead TTS Installation

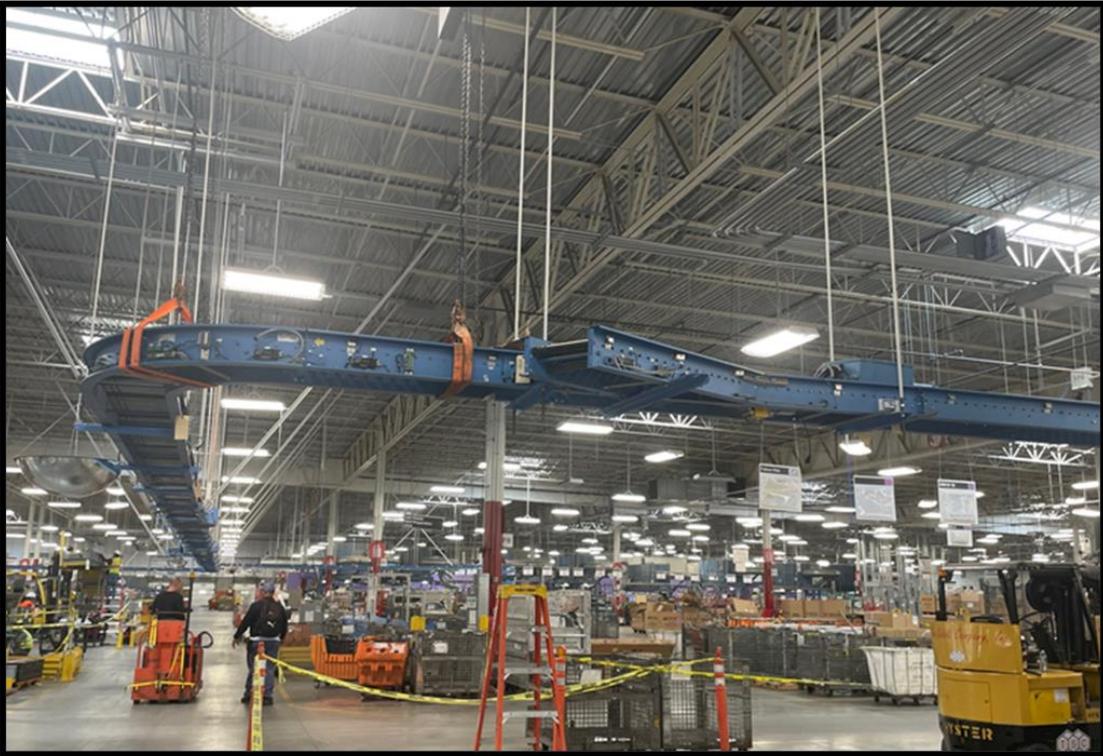


- Phase 1 Installation is underway

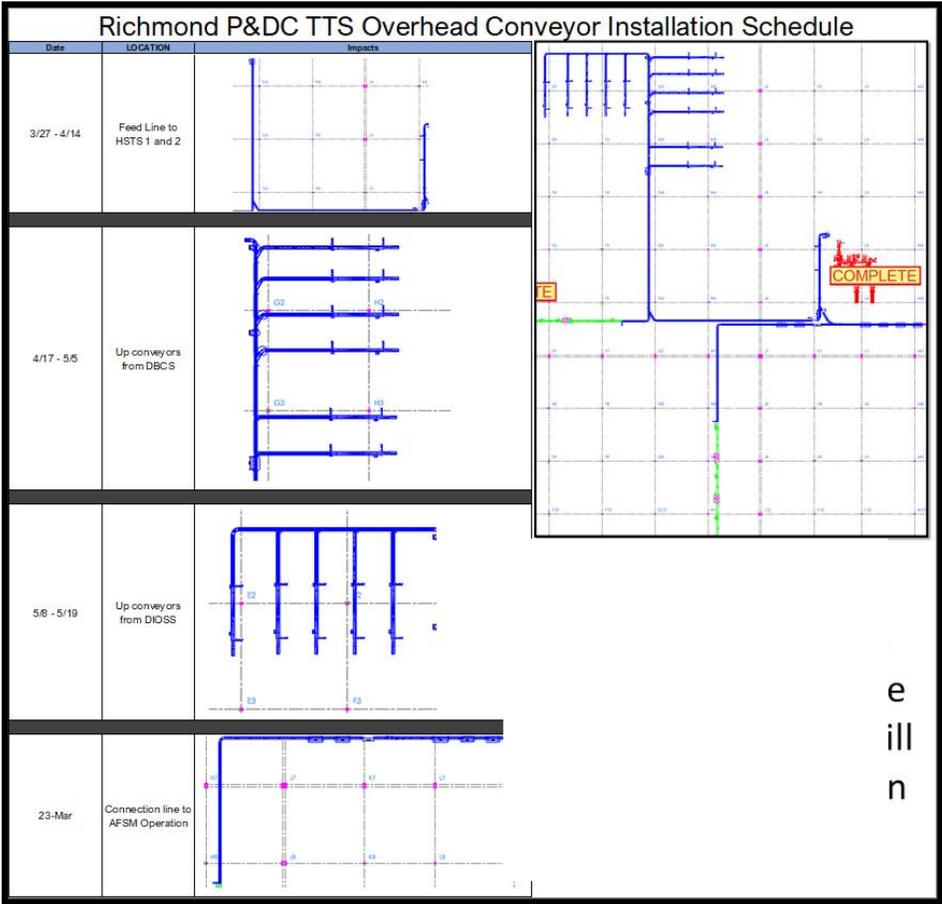

e  
ill  
n

# Richmond RPDC Transition Plan

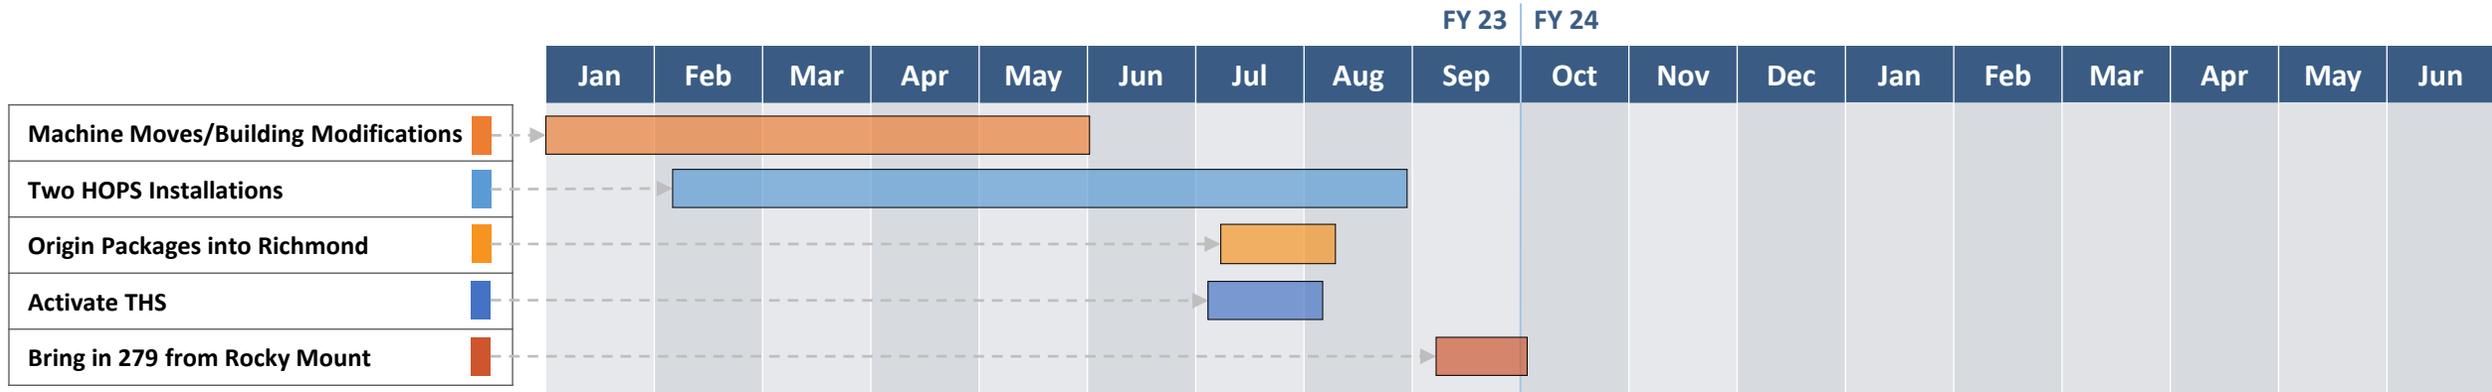

- Dec 2022 – May 2023: Machine removals and/or moves, to include building modifications
- Feb 2023 – Aug 2023: Installation and burn-in of the two HOPS machines
- Jul 2023: Bring in originating packages from Norfolk into Richmond RPDC
- Jul 2023: Continue processing destinating packages in Norfolk (pending 190 sort implementation)
- Jul 2023: Activate THS within Richmond RPDC
- Sep 2023: Bring in additional 3-digit (279) from Rocky Mount LPC

# Richmond VA - Processing Operations Transition/Implementation Status

## Completed Activities

--

## Upcoming Activities

<ul style="list-style-type: none"><li>• SWI training continues, on track for August completion for all 1,400 employees</li><li>• HOPS bid position plan developed</li><li>• Norfolk LPC mail move and equipment transition plan preliminary draft prepared</li></ul>
--

## Risks / Blocker / Activities Past Due

--

# Richmond RPDC Transition Plan

	New Bid Cluster	Bid Cluster 1	Bid Cluster 2	Bid Cluster 3	
<b>Current Bid Clusters</b>		Richmond PDC	Norfolk PDC	Rocky Mount PDF	
Richmond Bid Cluster	Bid Cluster	Finance #	Norfolk Bid Cluster	Bid Cluster	Finance #
LOG-RICHMOND VA P&DC	BC517650	517601	NOR-BERKLEY STA	BC516522	516517
RICHMOND VA MPA	BC517650	517646	NOR-DEBREE STA	BC516522	516518
RICHMOND VA P&DC	BC517650	517649	NOR-FLEET FSTA	BC516522	516519
RICHMOND PO	BC517650	517650	NOR-LAFAYETTE STA	BC516522	516520
RIC-AMPTHILL BR	BC517650	517655	NOR-NORVIEW STA	BC516522	516521
RIC-BELLEVUE BR	BC517650	517657	NORFOLK PO	BC516522	516522
RIC-BON AIR BR	BC517650	517659	NOR-OCEANVIEW STA	BC516522	516525
RIC-CAPITOL STA	BC517650	517660	NOR-PAGE STA	BC516522	516527
RIC-EAST END STA	BC517650	517661	NOR-THOMAS CORNER STA	BC516522	516529
RIC-FOREST HILL STA	BC517650	517663	NOR-WRIGHT STA	BC516522	516530
RIC-LAKESIDE BR	BC517650	517664	NOR-MILAN STA	BC516522	516531
RIC-MONTROSE HEIGHTS STA	BC517650	517665	LOG-NORFOLK VA P&DC	BC516522	516501
RIC-NORTHSIDE STA	BC517650	517666	NORFOLK VA P&DC	BC516522	516523
RIC-POCOSHOCK CREEK LANE B	BC517650	517667			
RIC-REGENCY BR	BC517650	517669	Rocky Mount Bid Cluster	Bid Cluster	Finance #
RIC-RIDGE BR	BC517650	517670	ROCKY MOUNT P&DF	BC366608	366610
RIC-SAUNDERS STA	BC517650	517671	ROCKY MOUNT PO	BC366608	366608
RIC-SOUTHSIDE STA	BC517650	517672	RKY-CARRIER ANX	BC366608	366609
RIC-STEWART STA	BC517650	517673			
RIC-WEST END STA	BC517650	517675			
RIC-WESTHAMPTON STA	BC517650	517676			

# **Atlanta Regional Processing & Distribution Center (RPDC)**

**PPM Design**

**Logistics Design**

**Processing & Maintenance Transition,  
Implementation, & Complement**


# PPM/Engineering US-R-0001 Atlanta Region

This region covers the greater Atlanta Metro Area handling the following 3-digit ZIP codes:

301, 302, 303, 311, 298, 308, 309, 304, 310, 312, 318, 319,  
300, 305, 306, 399

The Regional Processing and Distribution Center is a 1 million square foot USPS processing center building. There are four associated Local Processing Centers in the region comprised of repurposed existing facilities.


The RPDC Region is centered in Palmetto, Georgia.

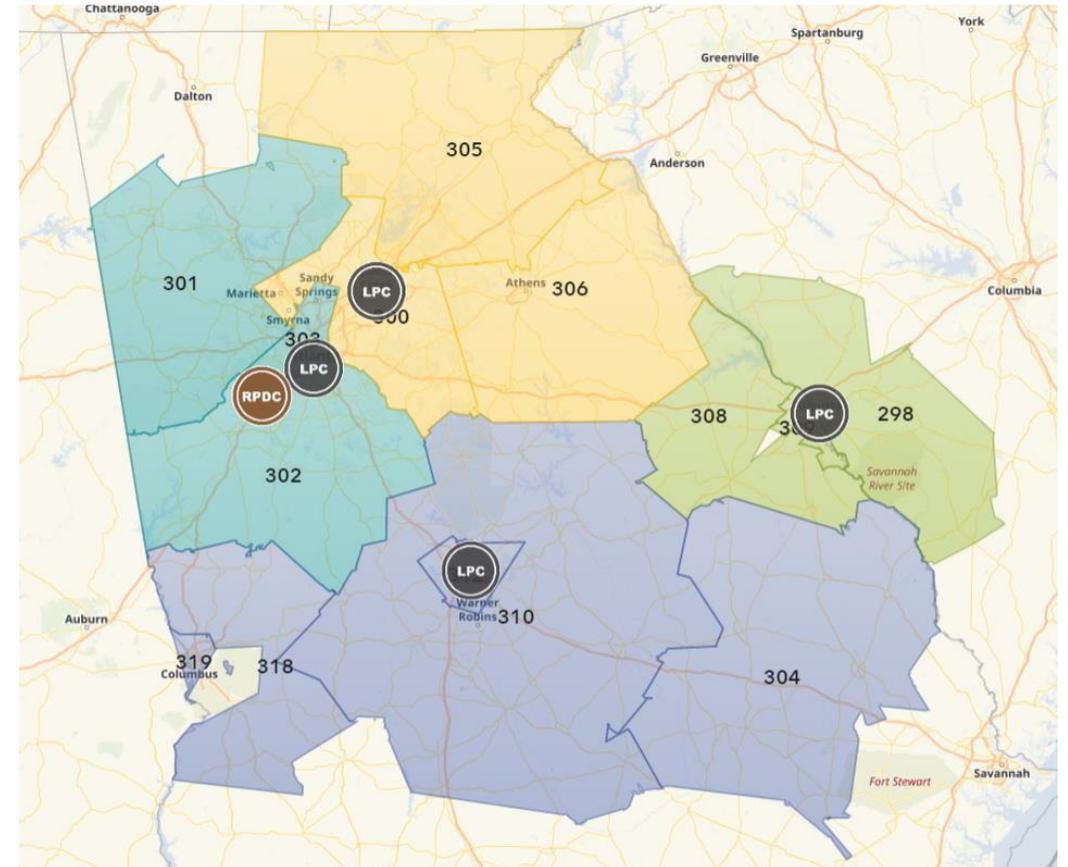

# Atlanta – New equipment and systems

- MaRS:
  - **Matrix Regional Sorter** – a new large sorting system for packages
  - Key components have started shipping to Georgia
    - Installation is being delayed by a few weeks to allow time for upgrades to the floor slab
- Loose Mail System (feeds the cancellation equipment) – installation has started
- Other material handling installs start in May

# Atlanta RPDC Transition Plan

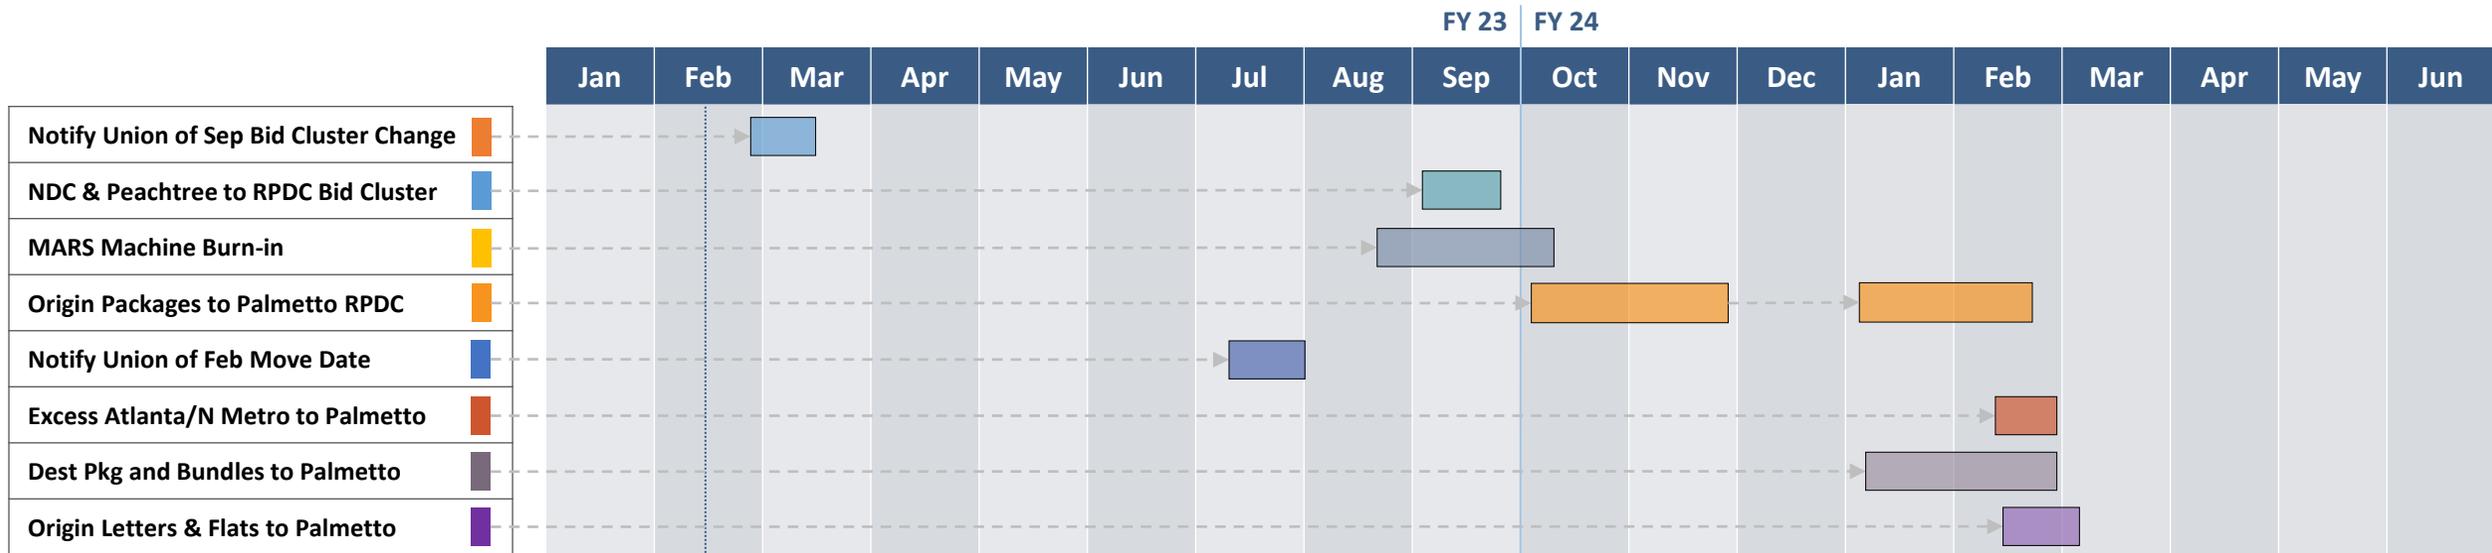

- Oct 2023 – Nov 2023: Originating Packages from N Metro P&DC Zips currently processed in Peachtree P&DC and Atlanta P&DC will be directed to Palmetto (approx. 50% of total Origin Packages) – Close PSA
- Oct 2023 – Nov 2023: Route NDC network trips into Palmetto, retain and process 30% and send remaining to Atlanta NDC
- Jan 2024 – Feb 2024: Remaining origin packages move from Peachtree P&DC to Palmetto – Close Peachtree
- Jan 2024 – Feb 2024: Remaining operations from Atlanta NDC move to Palmetto – Close NDC
- Jan 2024 – Feb 2024: Destinating Packages from N Metro P&DC, Atlanta P&DC, and Macon P&DC
- Feb 2024: Originating letters and flats from N Metro P&DC, Augusta P&DC, and Macon P&DC

# Atlanta GA - Processing Operations Transition/Implementation Status

## Completed Activities

--

## Upcoming Activities

- Mail move and people move proposal for Oct – Dec prepared, meeting scheduled with Mike and Dane – May 4

## Risks / Blocker / Activities Past Due

--

# Atlanta RPDC Transition Plan

	New Bid Cluster	Bid Cluster 1	Bid Cluster 1	Bid Cluster 2	Bid Cluster 3	Bid Cluster 4	Bid Cluster 4	Bid Cluster 5
<b>Current Bid Clusters</b>		Peachtree P&DC	Atlanta P&DC	North Metro	Atlanta NDC	Macon P&DC	Holt Annex	Augusta P&DC
<b>Future Bid Clusters</b>	Palmetto RPDC	closed	Atlanta P&DC	North Metro	closed	Macon LPC	closed	August LPC

Atlanta GA P&DC Bid Cluster (1)	Finance #	
ATHENS AUX VMF OF NORTH METRO GA	BC120440	120498
ATLANTA (NDC) AUX VMF OF ATLANTA GA	BC120440	120496
ATLANTA GA P&DC	BC120440	120441
ATLANTA GA VMF	BC120440	120443
ATLANTA MRC	BC120440	120405
ATLANTA PO	BC120440	120440
ATL-ATLANTA MPO	BC120440	120452
ATLANTA-CUSTOMER RETENTION	BC120440	120521
BROADVIEW AUX VMF OF NORTH METRO GA	BC120440	120497
DECATUR AUX VMF OF ATLANTA GA	BC120440	120493
LOG-ATLANTA GA P&DC	BC120440	120431
LOG-PEACHTREE GA P&DC	BC120440	120432
MSSC - ATLANTA GA PO	BC120440	121002
NORTH METRO GA VMF	BC120440	120446
<b>PEACHTREE GA P&amp;DC</b>	<b>BC120440</b>	<b>120442</b>
WEST END GA AUX VMF OF ATLANTA GA	BC120440	120494
All Atlanta Stations/Branches		

MACON GA P&DC Bid Cluster (4)	Finance #	
LOG-MACON GA P&DC	BC125489	125470
LOG-SOUTH MACON STATION	BC125489	125512
LOG-HOLT AVENUE ANNEX	BC125489	125521
MACON GA P&DC	BC125489	125490
<b>HOLT AVENUE ANNEX</b>	<b>BC125489</b>	<b>125501</b>
SOUTH MACON STATION	BC125489	125502
MACON GA VMF	BC125489	125491
MACON PO	BC125489	125489
MAC-PIO NONO STA	BC125489	125493
MAC-SOUTH MACON STA	BC125489	125495
MAC-ZEBULON BR	BC125489	125496
MAC-MAIN OFFICE STA	BC125489	125497
AUGUSTA AUX VMF OF GREENVILLE SC	BC125489	120492

Augusta GA Bid Cluster (5)	Finance #	
AUGUSTA GA P&DC	BC120473	120476
AUGUSTA PO	BC120473	120473
AUG-FOREST HILLS STA	BC120473	120487
AUG-MARTINEZ BR	BC120473	120488
AUG-PEACH ORCHARD STA	BC120473	120489
AUG-MAIN OFFICE STA	BC120473	120490

NDC Bid Cluster (3)	Finance #	
ATLANTA GA PSA	BC120439	120424
ATLANTA NDC	BC120439	120439
LOG-ATLANTA NDC	BC120439	120403
LOG-ATLANTA GA PSA	BC120439	120404

NORTH METRO GA P&DC Bid Cluster (2)	Finance #	
LOG-NORTH METRO GA P&DC	BC123569	123568
NORTH METRO GA P&DC	BC123569	123569

# **Chicago South Regional Processing & Distribution Center (RPDC)**

**PPM Design**

**Logistics Design**

**Processing & Maintenance Transition,  
Implementation, & Complement**


# PPM/Engineering US-R-0010 Chicago South IL

This region covers a portion of the the greater Chicago Metro Area handling the following 3-digit ZIP codes:


609, 613, 615, 617, 618, 090, 091, 092, 093, 094, 095, 096, 098, 099, 606, 607, 608, 962, 963, 964, 965, 966, 463, 464, 616, 604, 605

The Regional Processing and Distribution Center is housed in a converted NDC facility. There are five associated Local Processing Centers in the region comprised of repurposed existing facilities.

The RPDC Region is centered in Forest Park, Illinois

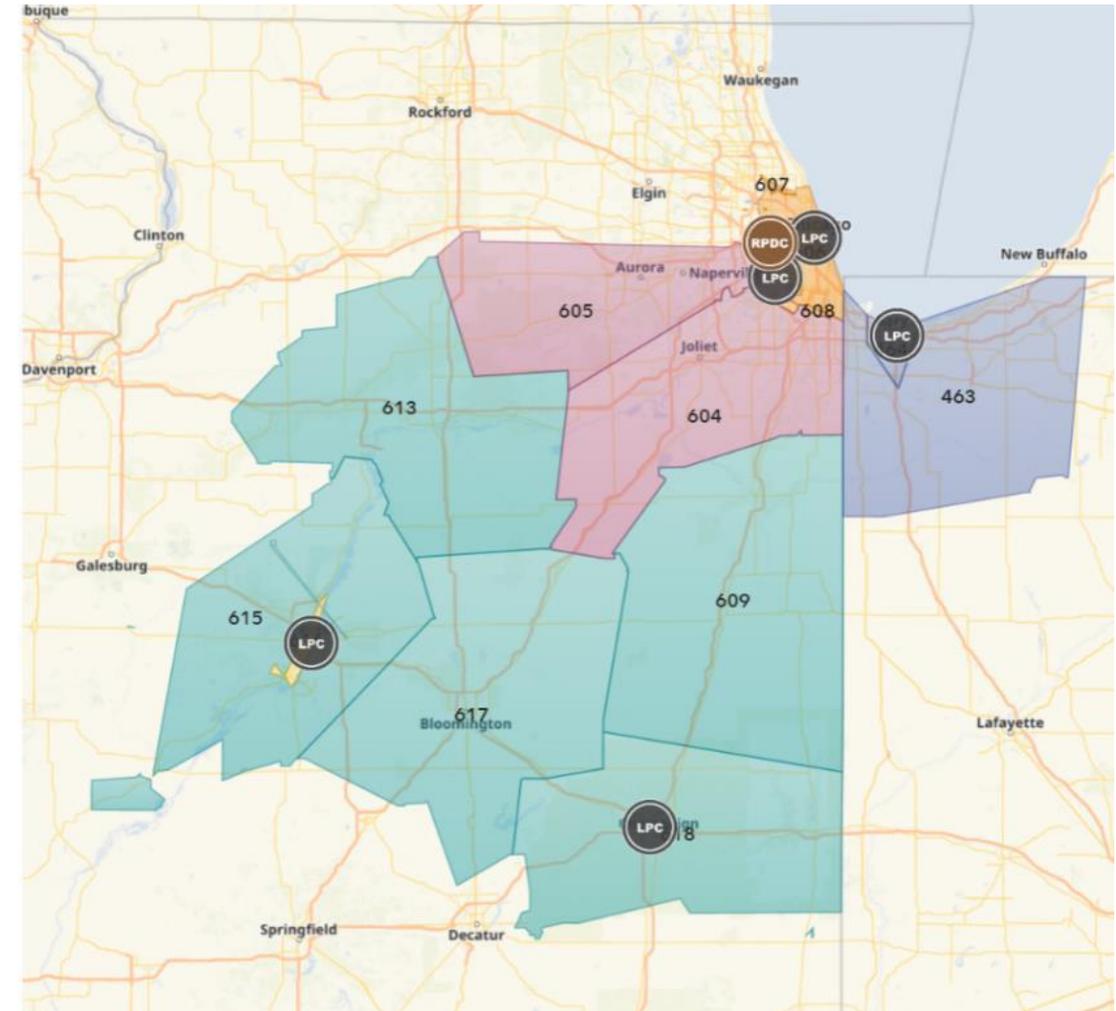

# Chicago South RPDC Transition Plan

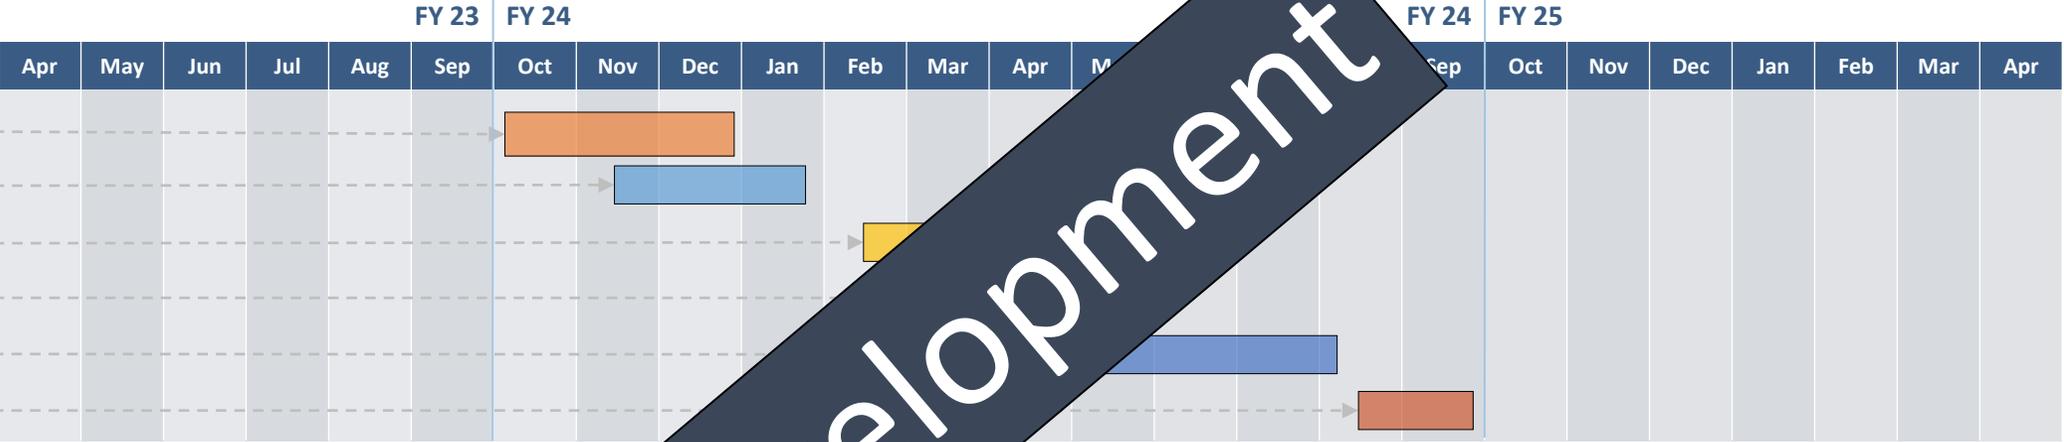

Under Development

# Chicago S IL – Processing Operations Transition/Implementation Status

## Completed Activities

- Post Matrix complement bid team met in Chicago, will finalize the plan 4/28/23

## Upcoming Activities

- Fall and peak mail move and people transition plan in development

## Risks / Blocker / Activities Past Due

# Chicago South RPDC Transition Plan

	New Bid Cluster	Bid Cluster 1	Bid Cluster 2	Bid Cluster 3	Bid Cluster 4	Bid Cluster 5	Bid Cluster 6	Bid Cluster 7	Bid Cluster 8
<b>Current Bid Clusters</b>		Chicago NDC	Cardiss Collins PDC	S. Suburban PDC	Fox Valley PDC	Busse PDC	Champaign PDC	Gary PDC	Peoria PDC
<b>Future Bid Clusters</b>									
<b>Chicago NDC Bid Cluster</b>	<b>Bid Cluster</b>	<b>Finance #</b>	<b>Bedford Park Bid Cluster</b>	<b>Bid Cluster</b>	<b>Finance #</b>	<b>Busse Bid Cluster</b>	<b>Bid Cluster</b>	<b>Finance #</b>	
CHICAGO NDC	BC161541	161541	BEDFORD PARK IL VMF	BC161544	161549	CHICAGO IL PSA	BC161128	161127	
LOG-CHICAGO NDC	BC161541	161641	CUSTOMER RELATIONS-ILLINOIS 2	BC161544	161887	BUSSE IL P&DC	BC161128	161128	
			ILLINOIS 2 DISTRICT	BC161544	161550	LOG-BUSSE IL P&DC	BC161128	161129	
<b>Chicago Bid Cluster</b>	<b>Bid Cluster</b>	<b>Finance #</b>	LOG-SOUTH SUBURBAN IL P&DC	BC161544	161646	LOG-CHICAGO IL PSA	BC161128	161130	
CHICAGO IL P&DC	BC161542	161547	BEDFORD PARK CFS	BC161544	166025				
CHICAGO IL VMF	BC161542	161538	SOUTH SUBURBAN IL P&DC	BC161544	161546	<b>Champaign Bid Cluster</b>	<b>Bid Cluster</b>	<b>Finance #</b>	
CHICAGO IL WESTERN AVE VMF	BC161542	161559	SOUTH SUBURBAN PO	BC161544	161544	CHAMPAIGN IL P&DC	BC161428	161430	
All Chicago Stations and Branches						CHAMPAIGN IL VMF	BC161428	161429	
			<b>Fox Valley Bid Cluster</b>	<b>Bid Cluster</b>	<b>Finance #</b>	BONDVILLE PO	BC161428	160840	
<b>Gary Bid Cluster</b>	<b>Bid Cluster</b>	<b>Finance #</b>	FOX VALLEY IL P&DC	BC162865	162865	CHAMPAIGN PO	BC161428	161428	
GARY IN P&DC	BC173168	173170	FOX VALLEY-CUSTOMER RETENTION	BC162865	160501	CHM-NEIL ST STA	BC161428	161431	
GARY IN VMF	BC173168	173167	LOG-FOX VALLEY IL P&DC	BC162865	162864	LOG-CHAMPAIGN IL P&DC	BC161428	161432	
GARY PO	BC173168	173168	MSSC - FOX VALLEY IL P&DC	BC162865	161001				
GRY-FSTA	BC173168	173171							
GRY-MILLER STA	BC173168	173172	<b>Peoria Bid Cluster</b>	<b>Bid Cluster</b>	<b>Finance #</b>				
GRY-TOLLESTON STA	BC173168	173173	LOG-PEORIA IL P&DC	BC166180	166189				
GRY-LAKE STA	BC173168	173174	PEORIA IL P&DC	BC166180	166182				
GRY-BRUNSWICK STA	BC173168	173175	PEORIA IL VMF	BC166180	166184				
GRY-GLEN PARK STA	BC173168	173176	PEORIA PO	BC166180	166180				
GRY-MERRILLVILLE BR	BC173168	173177	PEO-EAST PEORIA BR	BC166180	166181				
LOG-GARY IN P&DC	BC173168	173169	PEO-NO UNIVERSITY STA	BC166180	166183				
			PEO-WEST GLEN STA	BC166180	166185				
			PEO-PERSIMMON STREET STA	BC166180	166187				
			PEO-BARTONVILLE BR	BC166180	166188				



# **Houston Regional Processing & Distribution Center (RPDC)**

**Engineering Design**

**Logistics Design**

**Processing & Maintenance Transition,  
Implementation, & Complement**

# PPM/Engineering US-R-0003 Houston TX

This region covers the Houston Metro Areas handling the following 3-digit ZIP codes:

776, 777, 770, 772, 773, 774, 775, 778


The Regional Processing and Distribution Center in North Houston is slated for a minor rehabilitation.

Two associated Local Processing Centers in the region comprise repurposed existing facilities.

The RPDC Region is centered in North Houston, TX.



# Houston RPDC Transition Plan

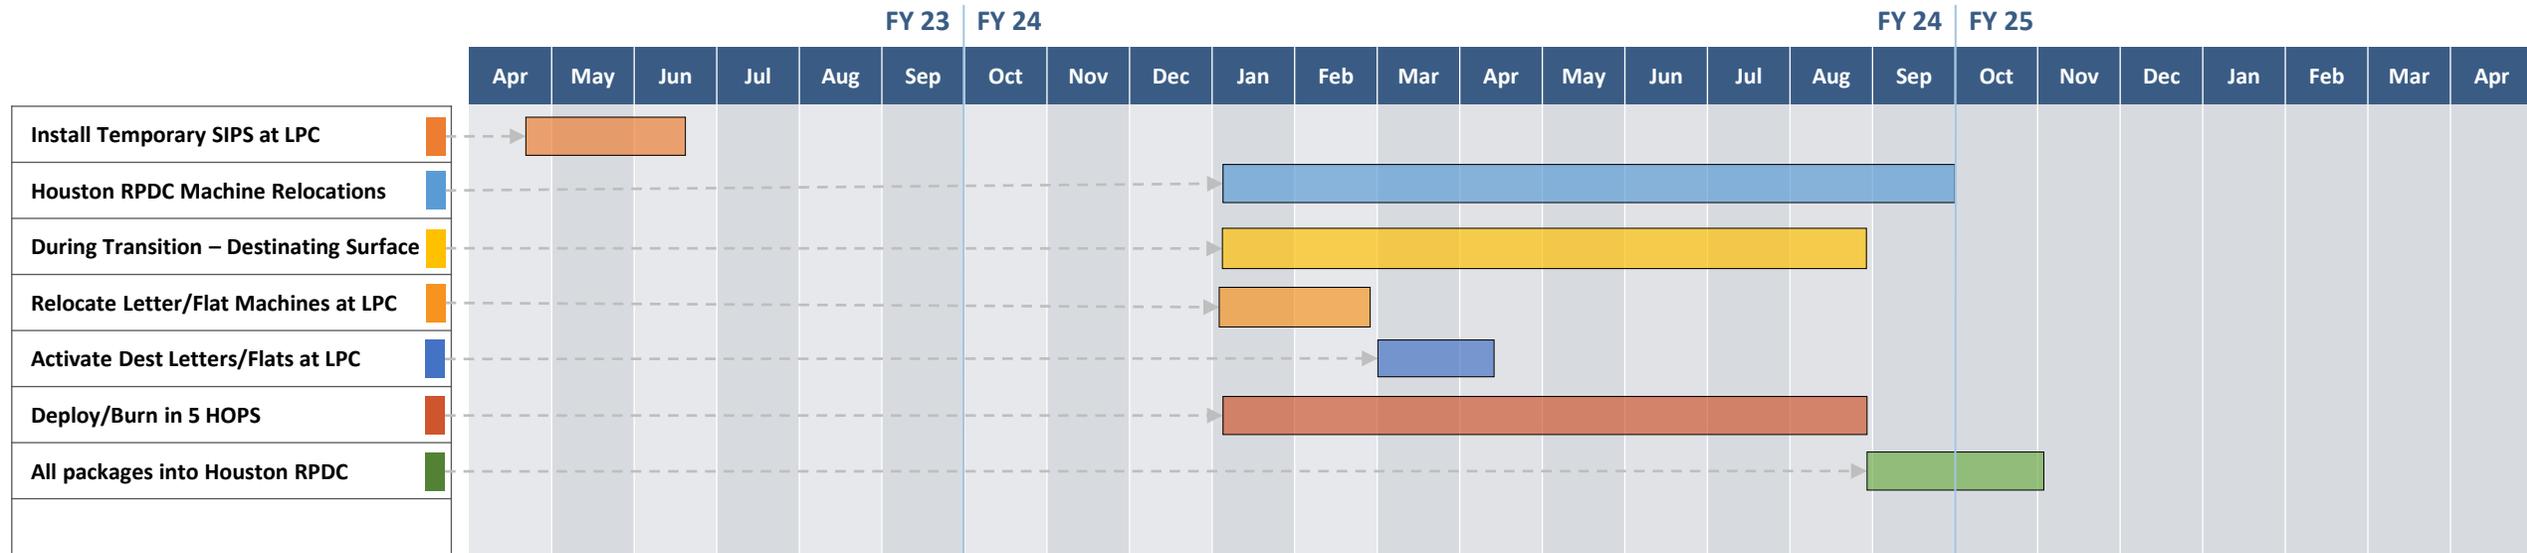

- Apr 2023 – Jun 2023: Install temporary SIPS machines to support the transition (machine relocations)
- Jan 2024 – Aug 2024: N Houston P&DC load level package volume between campus facilities during HOPS Installations
- Mar 2024 – Activate South Houston LPC and begin flowing letters and flats
- Jan 2024 – Aug 2024: N Houston Mail and package machine relocations and Installations
- Sep 2024 – Oct 2025: Transition all packages in Houston RPDC

# N Houston TX - Processing Operations Transition/Implementation Status

## Completed Activities

- Updates on Maintenance and Operations complement workbooks
- Collaboration with Facilities of planned timeline for S Houston availability for machine moves

## Upcoming Activities

- Vacate PSA by June - PSA SIPS & Spider storage and relocation needed for expiring PSA lease
- Updates on Maintenance and Ops workbooks continue as needed – specifically: complement allocation by equipment set, zero work hours and vacancy updates
- Finalizing "Float" plans for Automation and AFSM machines

## Risks / Blocker / Activities Past Due

# Houston RPDC Transition Plan

	New Bid Cluster	Bid Cluster	Bid Cluster 2
Current Bid Clusters		Beaumont PDF	N Houston P&DC
Future Bid Clusters			

Beaumont PDF	Bid Cluster	Finance #
BEAUMONT P&DF	BC480610	480612
LOG-BEAUMONT P&DF	BC480610	480699
BEAUMONT PO	BC480610	480610
BMT-DOWNTOWN STA	BC480610	480614
BMT-LUMBERTON STA	BC480610	480616
BMT-SOUTH END STA	BC480610	480613
BMT-TOBE HAHN STA	BC480610	480611

N HOUSTON TX P&DC	Bid Cluster	Finance #
HOUSTON N ANNEX	BC484143	484141
LOG-HOUSTON N ANNEX	BC484143	484101
HOU-CFS	BC484143	480375
LOG-N HOUSTON TX P&DC	BC484143	484102
LOG-NORTH HOUSTON TX PSA	BC484143	484103
N HOUSTON TX P&DC	BC484143	484143
NORTH HOUSTON TX PSA	BC484143	484157
NORTH ADMINISTRATIVE	BC484143	486475
TEXAS 2 DISTRICT	BC484143	484149

# **Indianapolis Regional Processing & Distribution Center (RPDC)**

**PPM Design**

**Logistics Design**

**Processing & Maintenance Transition,  
Implementation, & Complement**


# PPM/Engineering US-R-0012 Indianapolis IN

This region includes the communities from northeast Indiana, extending south to the capital of Indianapolis handling the following 3-digit ZIP codes:

467, 468, 460, 461, 462, 469, 472, 474, 478, 479, 473

The Regional Processing and Distribution Center in Indianapolis will be 1,000,000 sq feet of new construction for the USPS processing center building. There are three associated Local Processing Centers in the region comprised of repurposed existing facilities.

The RPDC Region is centered in Indianapolis, IN.

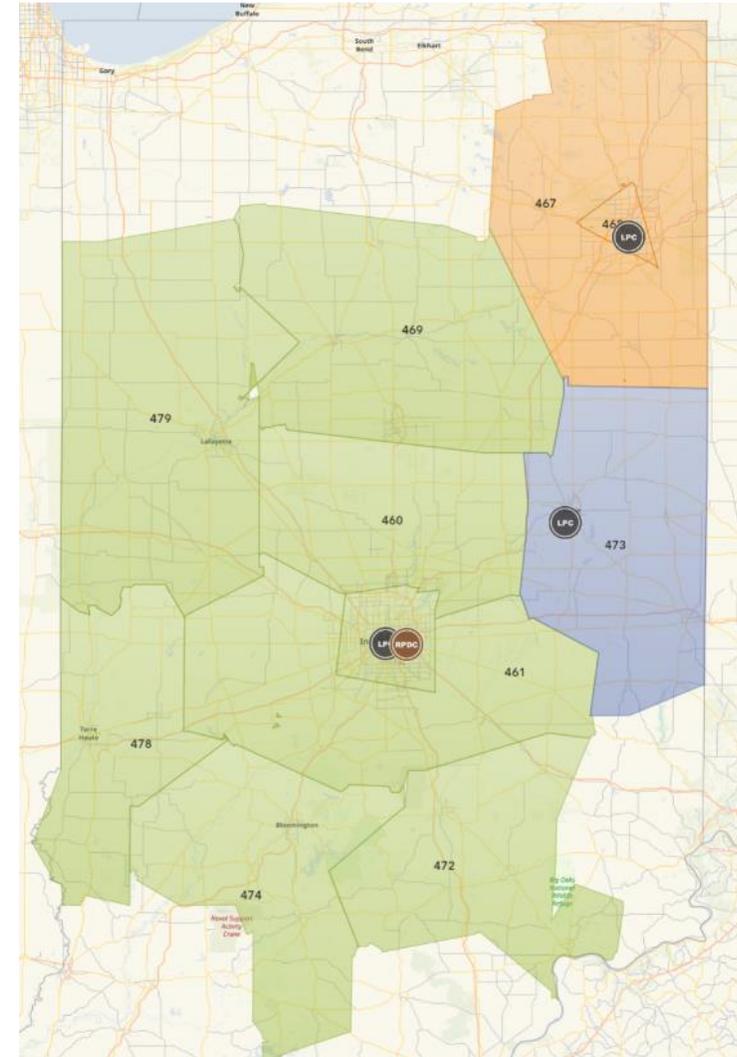

# Indianapolis RPDC Transition Plan



Timeline Update

# Indianapolis IN – Processing Operations Transition/Implementation Status

## Completed Activities

- EAS Maintenance Training chart filled and scheduling for 100% completion.
- Working with Purchasing on maintenance equipment needed.
- Cataloging machine specifics on current machine set. (LAU2, Phases, etc)

## Upcoming Activities

- Evaluation of RPDC staffing vs. current total

## Risks / Blocker / Activities Past Due

# Indianapolis RPDC Transition Plan

	New Bid Cluster	Bid Cluster 1	Bid Cluster 2	Bid Cluster 3
Current Bid Clusters		FT WAYNE IN P&DC	MUNCIE IN P&DF	INDIANAPOLIS IN P&DC
Future Bid Clusters				

Fort Wayne P&DC	Bid Cluster	Finance #
FORT WAYNE PO	BC172915	172915
FWA-GABRIEL STA	BC172915	172916
FORT WAYNE IN VMF	BC172915	172917
FWA-CENTENNIAL STA	BC172915	172918
FWA-DIPLOMAT PLAZA STA	BC172915	172919
FT WAYNE IN P&DC	BC172915	172920
FWA-HAZELWOOD STA	BC172915	172921
FWA-NORTHWOOD STA	BC172915	172922
FWA-WAYNE DALE STA	BC172915	172923
LOG-FT WAYNE IN P&DC	BC172915	172924
FWA-ST MARY STA	BC172915	172960

Muncie P&DF	Bid Cluster	Finance #
MUNCIE PO	BC175907	175907
MUNCIE P&DF	BC175907	175909
OAKVILLE PO	BC175907	176479
SELMA PO	BC175907	177964

Indianapolis P&DC	Bid Cluster	Finance #
IND-BRIDGEPORT BR	BC174037	170224
IND-BACON STA	BC174037	170430
IND-BRIGHTWOOD STA	BC174037	170846
IND-BROAD RIPPLE STA	BC174037	170885
MSSC - INDIANAPOLIS IN PO	BC174037	171002
IND-CASTLETON BR	BC174037	171308
IND-CIRCLE CITY STA	BC174037	171556
IND-CLERMONT BR	BC174037	171627
IND-INDIANAPOLIS CFS	BC174037	171798
IND-CUMBERLAND BR	BC174037	172091
IND-EAGLE CREEK BR	BC174037	172397
IND-EASTGATE STA	BC174037	172410
INDIANAPOLIS STC	BC174037	172430
IND-GARFIELD STA	BC174037	173151
INDIANAPOLIS IN PSA	BC174037	174028
LOG-INDIANAPOLIS MPA	BC174037	174029
INDIANAPOLIS MPA	BC174037	174031
INDIANA DISTRICT	BC174037	174035
INDIANAPOLIS IN VMF	BC174037	174036
INDIANAPOLIS PO	BC174037	174037
INDIANAPOLIS IN P&DC	BC174037	174038
HIGH SCHOOL RD MAIL PROCESSING ANNEX	BC174037	174040
MUNCIE AUX VMF OF INDIANAPOLIS IN	BC174037	174044
LAFAYETTE AUX VMF OF INDIANAPOLIS IN	BC174037	174045
NORA IN VMF	BC174037	174046
LOG-INDIANAPOLIS IN P&DC	BC174037	174058
LOG-HIGH SCHOOL RD MAIL PROCESSING ANNEX	BC174037	174060
LOG-INDIANAPOLIS IN PSA	BC174037	174068
IND-LAWRENCE BR	BC174037	174669
IND-LINWOOD STA	BC174037	174900
IND-MOW SVC	BC174037	175087
IND-MAPLETON STA	BC174037	175103
LOG-MUNCIE P&DF	BC174037	175910
IND-NEW AUGUSTA BR	BC174037	175994
IND-NORA BR	BC174037	176308
IND-OAKLANDON BR	BC174037	176456
IND-PARK FLETCHER BR	BC174037	176737
IND-RAINBOW STA	BC174037	177210
IND-SOUTHPORT BR	BC174037	178201
IND-SPEEDWAY BR	BC174037	178238
IND-WANAMAKER BR	BC174037	179151
IND-WEST INDIANAPOLIS STA	BC174037	179300



# **Portland Regional Processing & Distribution Center (RPDC)**

**Engineering Design**

**Logistics Design**

**Processing & Maintenance Transition,  
Implementation, & Complement**


# PPM/Engineering US-R-0007 Portland OR

This region includes the communities from Medford, OR, extending north into the greater Portland, Oregon Metro Area, handling the following 3-digit ZIP codes:

974, 975, 976, 970, 971, 972, 973, 977, 978, 986

The Regional Processing and Distribution Center is a recent USPS processing center building, and is one of the largest facilities in the country. There are three associated Local Processing Centers in the region comprised of repurposed existing facilities.

The RPDC Region is centered in Portland, OR

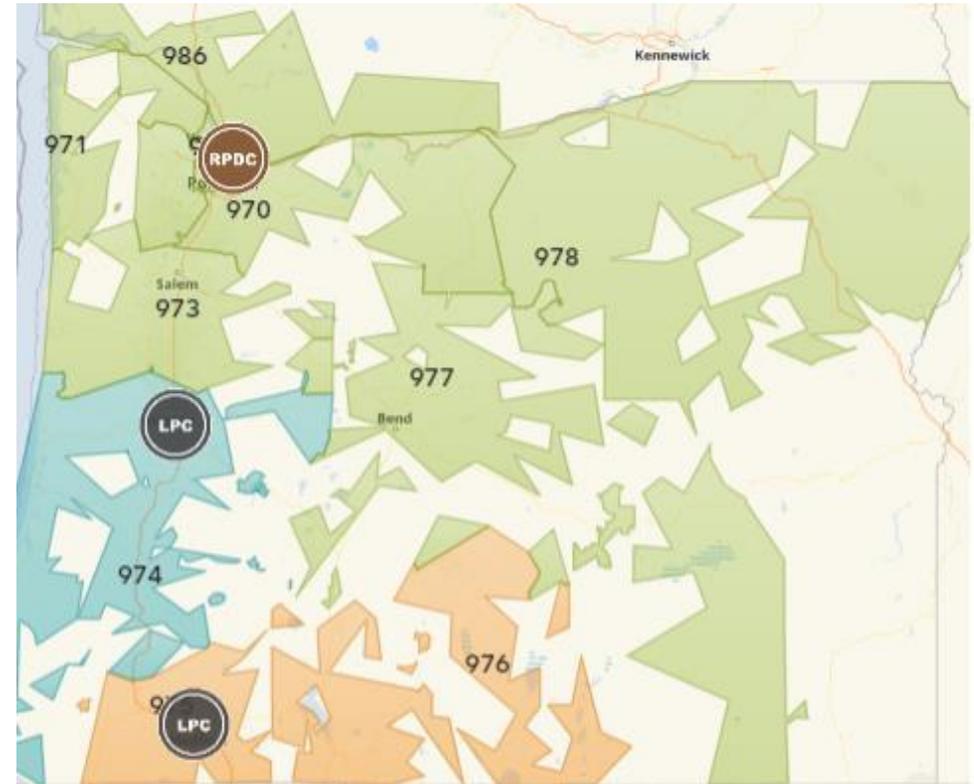

# Portland RPDC Transition Plan



Timeline Update

# Portland OR – Processing Operations Transition/Implementation Status

## Completed Activities

- 70% Design approved 4/26/2023

## Upcoming Activities

- Preliminary mail move and people transition plan in development
- 100% Design schedule for 6/2/23

## Risks / Blocker / Activities Past Due

# Portland RPDC Transition Plan

	New Bid Cluster	Bid Cluster 1	Bid Cluster 2	Bid Cluster 3	
<b>Current Bid Clusters</b>		Portland PDC	Eugene PDC	Medford PDC	
<b>Future Bid Clusters</b>					
Portland	Bid Cluster	Finance #	Eugene Bid Cluster	Bid Cluster	Finance #
ID-MT-OR DISTRICT	BC406784	406787	EUGENE OR P&DC	BC402848	402850
LOG-PORTLAND OR P&DC	BC406784	406782	EUGENE OR VMF	BC402848	402849
MSSC - PORTLAND OR PO	BC406784	401000	EUGENE PO	BC402848	402848
PORTLAND OR P&DC	BC406784	406785	EUG-RIVER ROAD STA	BC402848	402851
POR-AIRPORT RETAIL STA	BC406784	406754	EUG-WESTSIDE STA	BC402848	402852
POR-EAST PORTLAND STA	BC406784	406755	EUG-SOUTHSIDE STA	BC402848	402854
POR-MILWAUKIE BR	BC406784	406757	EUG-MAIN OFFICE STA	BC402848	402855
POR-TIGARD BR	BC406784	406758	PORTLAND OR VMF	BC402848	406786
POR-BROOKLYN STA	BC406784	406759	SALEM OR VMF	BC402848	407393
POR-WATERFRONT STA	BC406784	406760			
POR-SOUTHWEST PORTLAND DCU	BC406784	406761			
POR-CENTRAL STA	BC406784	406762			
POR-KENTON STA	BC406784	406763			
POR-ROSE CITY PARK STA	BC406784	406764			
POR-WEST SLOPE BR	BC406784	406765	Medford Bid Cluster	Bid Cluster	Finance #
POR-EASTPORT (LENDS) RETAIL ANX	BC406784	406766	LOG-MEDFORD OR P&DC	BC405408	405407
POR-OAK GROVE BR	BC406784	406767	MEDFORD OR P&DC	BC405408	405409
POR-MIDWAY STA	BC406784	406768	MEDFORD PO	BC405408	405408
POR-PARKROSE STA	BC406784	406769	MED-CENTRAL POINT BR	BC405408	405410
POR-CRESTON STA	BC406784	406770	MED-WHITE CITY BR	BC405408	405411
POR-PIEDMONT STA	BC406784	406772	MED-CARRIER ANNEX	BC405408	405412
POR-SELLWOOD RETAIL STA	BC406784	406773			
POR-RIVER DISTRICT DCU	BC406784	406774			
POR-MULTNOMAH STA	BC406784	406775			
POR-LENDS DCU	BC406784	406776			
POR-HOLLADAY PARK STA	BC406784	406777			
POR-ST JOHNS STA	BC406784	406778			
POR-SELLWOOD DCU	BC406784	406779			
PORTLAND PO	BC406784	406784			
POR-MAIN OFFICE RETAIL STA	BC406784	406790			
PORTLAND-CUSTOMER RETENTION	BC406784	400501			
VANCOUVER AUX VMF OF PORTLAND OR	BC406784	540547			

# **Charlotte Regional Processing & Distribution Center (RPDC)**

**PPM Design**

**Logistics Design**

**Processing & Maintenance Transition,  
Implementation, & Complement**


# PPM/Engineering US-R-0008 Charlotte NC

This region covers the greater Charlotte Metro Area handling the following 3-digit ZIP codes:

280, 281, 282, 286, 297, 287, 288, 289, 293, 296, 242, 246, 376

The Regional Processing and Distribution Center is a 1 million square foot USPS processing center building. There are three associated Local Processing Centers in the region comprised of repurposed existing facilities.

The RPDC Region is centered in Gastonia, North Carolina.

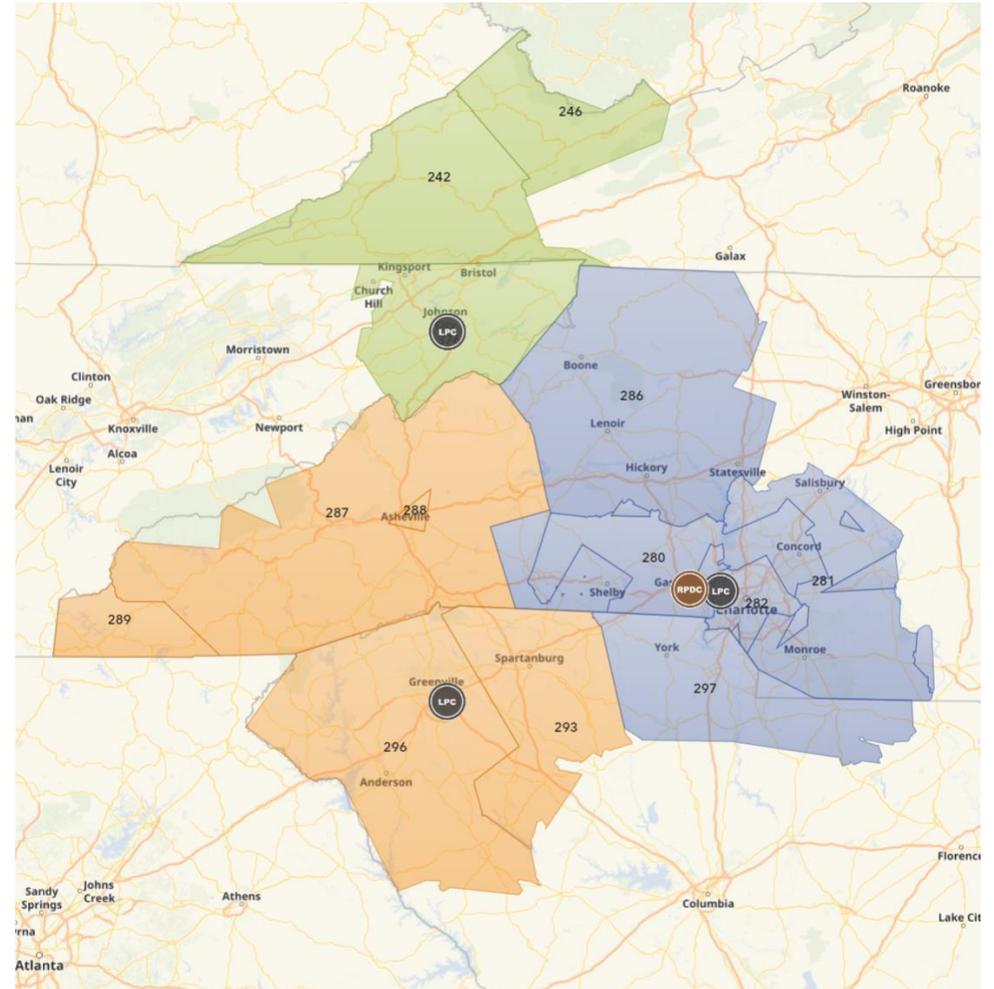

# Charlotte RPDC Transition Plan



- Aug 2023 – Jan 2024: Install and burn-in five HOPS machines
- Sep 2023 – Oct 2023: Install USS XL machine
- Oct 2023 – Nov 2023: Move 100K outgoing package volume from Mid-C into Charlotte RPDC
- Nov 2023: Move 10K non-machinable outside package from Mid-C into Charlotte RPDC
- Jan 2024 – Feb 2024: Move remaining package volume from Mid-C into Charlotte RPDC
- Feb 2024 – Mar 2024: Activate THS
- Mar 2024 – Feb 2024: Move machines into, within, and/or out of Mid-C LPC
- May 2024 – Jun 2024: Move destinating letters and flats into Mid-C LPC



# Charlotte NC – Processing Operations Transition/Implementation Status

Completed Activities

Upcoming Activities
<ul style="list-style-type: none"><li>• Fall and peak mail move and people transition plan in development</li><li>• Post matrix bids expected by 5/10/23</li></ul>

Risks / Blocker / Activities Past Due

# Charlotte RPDC Transition Plan

	New Bid Cluster	Bid Cluster 1	Bid Cluster 2	Bid Cluster 3	
<b>Current Bid Clusters</b>		Charlotte PDC	Greenville, SC PDC	Johnson City, TN PDC	
		Mid-Carolina PDC			
<b>Future Bid Clusters</b>					
<b>Charlotte, NC</b>	Bid Cluster	Finance #	Greenville Bid Cluster	Bid Cluster	Finance #
CHARLOTTE NC P&DC	BC361392	361393	ASHEVILLE AUX VMF OF GREENVILLE SC	BC453620	361409
CHARLOTTE NC VMF	BC361392	361396	GVL-STATION A	BC453620	450217
CHARLOTTE PO	BC361392	361392	GVL-PARK PLACE BR	BC453620	450218
CLT- NORTH TRYON STA	BC361392	361398	GREENVILLE PO	BC453620	453620
CLT-W T HARRIS STA	BC361392	361399	GVL-CALVIN STREET ANX	BC453620	453623
CLT-ARROWOOD STA	BC361392	361400	GVL-KEITH D OGLESBY STA	BC453620	453624
CLT-MINT HILL STA	BC361392	361401	GVL-PLEASANTBURG STA	BC453620	453625
CLT-IDLEWILD CARRIER ANX	BC361392	361402	GVL-BEREA BR	BC453620	453626
CLT-INDEPENDENCE CARRIER ANX	BC361392	361403	GREENVILLE SC MPA	BC453620	453619
CLT-MINJET CARRIER ANX	BC361392	361404	GREENVILLE SC P&DC	BC453620	453621
CLT-NORTHEAST STA	BC361392	361405	GREENVILLE SC VMF	BC453620	453622
CLT-CARMEL STA	BC361392	361406	LOG-GREENVILLE SC P&DC	BC453620	453601
CLT-BALLANTYNE STA	BC361392	361407	LOG-GREENVILLE SC MPA	BC453620	453602
CLT-PLAZA STA	BC361392	361411	SPARTANBURG AUX VMF OF GREENVILLE SC	BC453620	453628
CLT-PARK ROAD ANX	BC361392	361412			
CLT-STEELE CREEK STA	BC361392	361413	Johnson City Bid Cluster	Bid Cluster	Finance #
CLT-OAKDALE STA	BC361392	361414	JOHNSON CITY PO	BC474476	474476
CLT-FREEDOM STA	BC361392	361415	JOH-GRAY BR	BC474476	474477
CLT-30TH STREET STA	BC361392	361416	JOH-CARROLL REESE STA	BC474476	474478
CLT-RANDOLPH STA	BC361392	361417	JOHNSON CITY TN P&DC	BC474476	474474
CLT-DOWNTOWN STA	BC361392	361418			
CLT-YORKMONT STA	BC361392	361419			
HICKORY AUX VMF OF CHARLOTTE NC	BC361392	368718			
LOG-CHARLOTTE NC P&DC	BC361392	361389			
LOG-MID CAROLINA NC P&DC	BC361392	361421			
LOG-MID CAROLINA NC PSA	BC361392	361422			
MID CAROLINA NC P&DC	BC361392	361420			
MID CAROLINA NC PSA	BC361392	361425			
MID-CAROLINAS DISTRICT	BC361392	361395			
MSSC - CHARLOTTE NC PO	BC361392	361002			
NORTH CAROLINA DISTRICT	BC361392	363197			
GASTONIA PO	BC362912	362912			
GAS-NEW HOPE ANX	BC362912	362914			



# **Jacksonville Regional Processing & Distribution Center (RPDC)**

**PPM Design**

**Logistics Design**

**Processing & Maintenance Transition,  
Implementation, & Complement**


# PPM/Engineering US-R-0025 Jacksonville FL

This region covers Jacksonville, FL Area handling the following 3-digit ZIP codes:

313, 314, 315, 320, 322, 326, 344, 316, 317, 323, 398

The Regional Processing and Distribution Center is an existing USPS processing center building. There are two associated Local Processing Centers in the region comprised of repurposed existing facilities.

The RPDC Region is centered in Jacksonville, FL

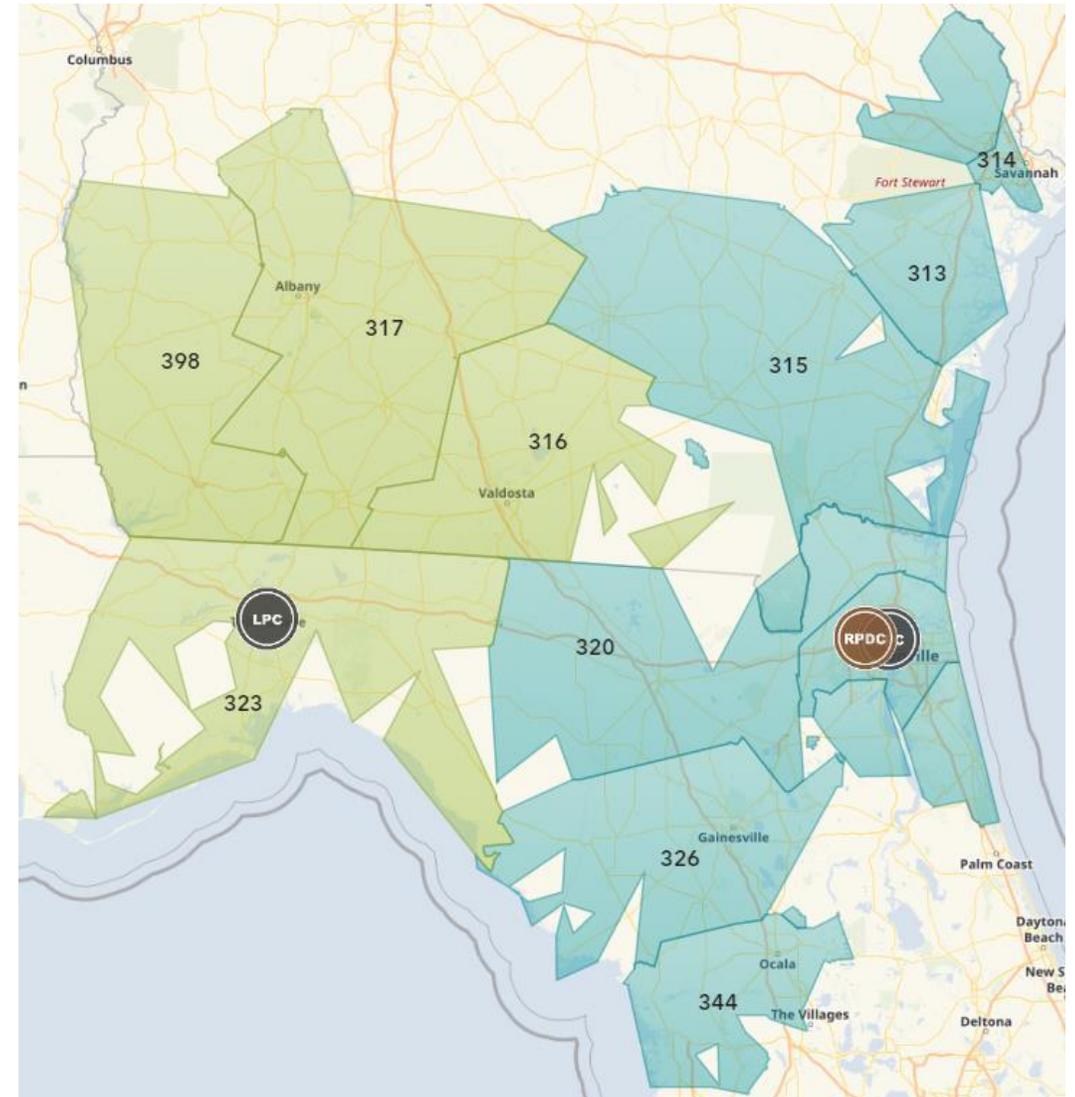

# Jacksonville RPDC Transition Plan



**Timeline Update**

# Jacksonville FL – Processing Operations Transition/Implementation Status

## Completed Activities

- F1 Complement Baseline completed
- 24/30 month pre-career conversion projection prepared

## Upcoming Activities

- F1 and F3b Matrices per LMOU sections to be prepared
- RCS removal to begin
- APBS and SIPS relocations

## Risks / Blocker / Activities Past Due

# Jacksonville RPDC Transition Plan

	New Bid Cluster	Bid Cluster 1	Bid Cluster 2	Bid Cluster 3	Bid Cluster 4
Current Bid Clusters		GAINESVILLE FL P&DF	JACKSONVILLE FL P&DC	JACKSONVILLE NDC	TALLAHASSEE FL P&DC
Future Bid Clusters					

Gainesville PDF	Bid Cluster	Finance #
GAINESVILLE P&DF	BC113225	113250
GNV - NORTHWEST STA	BC113225	113224
GAINESVILLE PO	BC113225	113225
GNV-DOWNTOWN STA	BC113225	113226
GNV-GMF STA	BC113225	113227
GNV-MAIN ST STA	BC113225	113228
GNV-UNIVERSITY STA	BC113225	113229
GAINESVILLE S&DC (SORTING & DELIVERY CENTER)	BC113225	113230

Jacksonville NDC	Bid Cluster	Finance #
JACKSONVILLE NDC	BC114381	114381
JACKSONVILLE FL PSA	BC114381	114394
LOG-JACKSONVILLE NDC	BC114381	114325
LOG-JACKSONVILLE FL PSA	BC114381	114326
Tallahassee PDC	Bid Cluster	Finance #
LOG-TALLAHASSEE FL P&DC	BC118895	118899
TALLAHASSEE FL P&DC	BC118895	118898
TLH-CENTERVILLE STA	BC118895	118891
TLH-GMF STA	BC118895	118892
TLH-LAKE JACKSON STA	BC118895	118893
TLH-WESTSIDE STA	BC118895	118894
TALLAHASSEE PO	BC118895	118895
TLH - LEON STA	BC118895	118896

Jacksonville PDC	Bid Cluster	Finance #
FLORIDA 1 DISTRICT	BC114380	114384
GAINESVILLE AUX VMF OF JACKSONVILLE FL	BC114380	114387
GFA DISTRICT CRAFT	BC114380	114351
JACKSONVILLE FL P&DC	BC114380	114382
JACKSONVILLE FL VMF	BC114380	114383
JACKSONVILLE PO	BC114380	114380
JAX-ARLINGTON STA	BC114380	114400
JAX-ATLANTIC BCH STA	BC114380	114401
JAX-BALDWIN STA	BC114380	114402
JAX-BAYMEADOWS DDC	BC114380	114403
JAX-CARVER STA	BC114380	114404
JAX-CFS	BC114380	114406
JAX-GMF MAIN OFC PSTL STR	BC114380	114407
JAX-JAX BEACH STA	BC114380	114408
JAX-LAKE FOREST STA	BC114380	114409
JAX-LAKE SHORE STA	BC114380	114410
JAX-MANDARIN PSTL STR	BC114380	114411
JAX-MONUMENT PSTL STR	BC114380	114413
JAX-MURRAY HILL STA	BC114380	114414
JAX-GATEWAY CARRIER ANX	BC114380	114415
JAX-NAS MAYPORT FSTA	BC114380	114416
JAX-NAVAL AIR FSTA	BC114380	114417
JAX-NORTH JAX STA	BC114380	114418
JAX-NW ST JOHNS FSTA	BC114380	114419
JAX-POTTSBURG PSTL STR	BC114380	114420
JAX-SOUTH JAX STA	BC114380	114421
JAX-SOUTHPOINT PSTL STR	BC114380	114422
JAX-EDDIE MAE STEWARD FSTA	BC114380	114423
JAX-WESTLAND PSTL STR	BC114380	114424
LOG-JACKSONVILLE FL P&DC	BC114380	114393
TALLAHASSEE AUX VMF OF JACKSONVILLE FL	BC114380	114389

# **Boise Regional Processing & Distribution Center (RPDC)**

**Engineering Design**

**Logistics Design**

**Processing & Maintenance Transition,  
Implementation, & Complement**


# PPM/Engineering US-R-0052 Boise ID

This region covers the Boise, ID Area handling the following 3-digit ZIP codes:

833, 836, 837, 979, 832, 834

The Regional Processing and Distribution Center is an existing USPS processing center building. There are two associated Local Processing Center in the region comprised of a repurposed facility.

The RPDC Region is centered in Boise, ID.

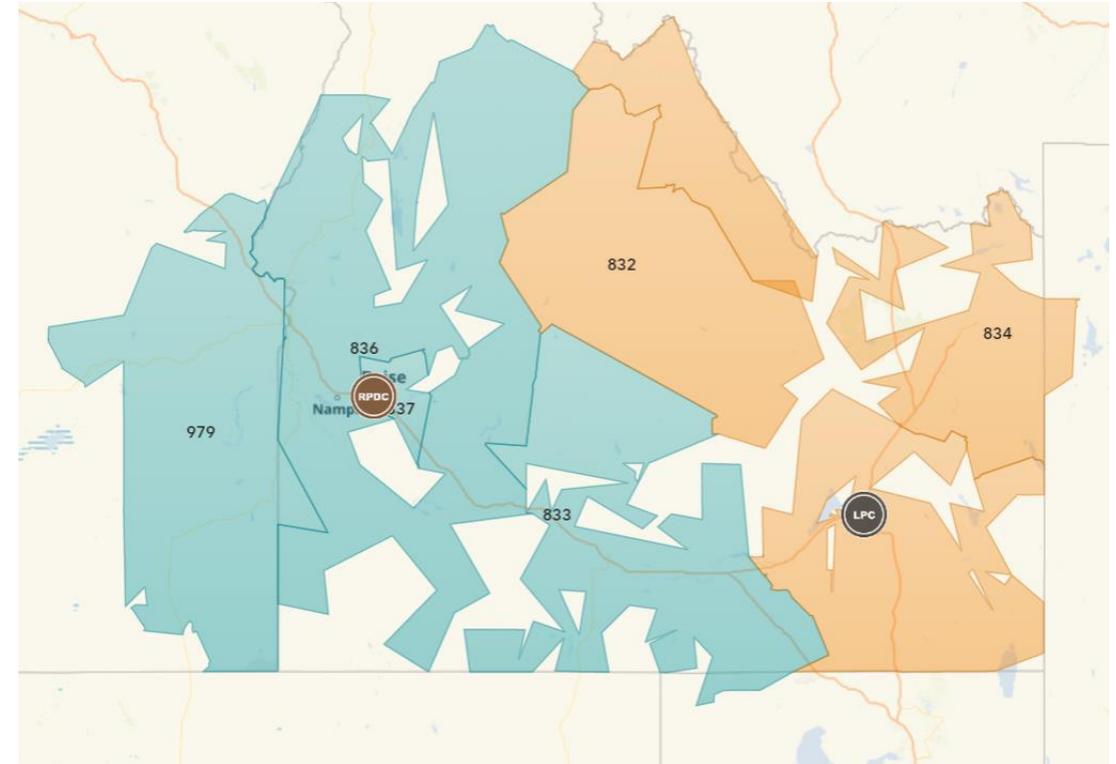

# Boise RPDC Transition Plan



Timeline Update

# Boise ID – Processing Operations Transition/Implementation Status

## Completed Activities

- Updates to complement workbook
- Reversions processed to baseline complement
- Identified stacker modules needed for 2 DBCS machines

## Upcoming Activities

- 70% Design Meeting Scheduled for 4/28
- Logistics and Operations joint meeting on Mail Move for 832/834 volumes

## Risks / Blocker / Activities Past Due

# Boise RPDC Transition Plan

	New Bid Cluster	Bid Cluster 1	Bid Cluster 2
Current Bid Clusters		BOISE ID P&DC	POCATELLO ID P&DF
Future Bid Clusters			

Boise	Bid Cluster	Finance #
BOISE ID P&DC	BC150925	150926
BOISE ID VMF	BC150925	150927
BOISE PO	BC150925	150925
BOI-FIVE MILE STA	BC150925	150929
BOI-BORAH STA	BC150925	150930
BOI-COLE VILLAGE	BC150925	150931
BOI-COLLISTER STA	BC150925	150932
BOI-GARDEN CITY STA	BC150925	150933
BOI-OREGON TRAIL STA	BC150925	150934
BOI-OVERLAND STA	BC150925	150935
BOI-MAIN OFFICE STA	BC150925	150936
LOG-BOISE ID P&DC	BC150925	150916

Pocatello	Bid Cluster	Finance #
POCATELLO MPF	BC157225	157228
POCATELLO PO	BC157225	157225
POC-BANNOCK STA	BC157225	157226
POC-GATEWAY STA	BC157225	157227

# **Greensboro Regional Processing & Distribution Center (RPDC)**

**PPM Design**

**Logistics Design**

**Processing & Maintenance Transition,  
Implementation, & Complement**


# PPM/Engineering US-R-0004 Greensboro NC

This region covers the greater Greensboro, Fayetteville, and Raleigh, North Carolina Metro Areas. It also covers the southwestern Roanoke, Virginia, area. The following 3-digit ZIP codes are included

283, 284, 285, 270, 271, 272, 273, 274, 275, 276, 277, 278,  
240, 241, 243, 245, 247

The Greensboro, NC Regional Processing and Distribution Center is an existing USPS processing center building suited for a significant expansion. The future target addition requires approximately 500,000 square feet. There are five associated Local Processing Centers in the region comprised of repurposed existing facilities.

The RPDC Region is centered in Greensboro, NC 3701 W Wendover Ave, Greensboro, NC 27495.

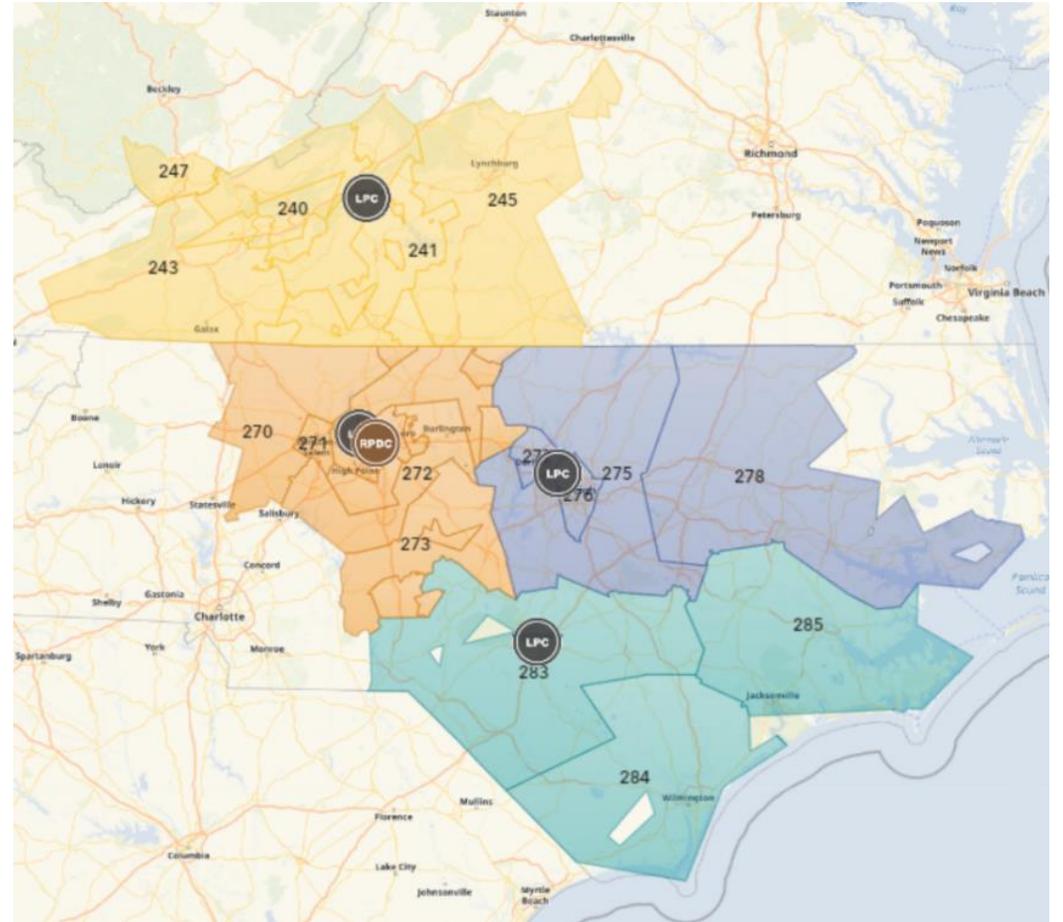

# Greensboro RPDC Transition Plan



Timeline Update

# Greensboro NC - Processing Operations Transition/Implementation Status

## Completed Activities

- Site Specific HR/LR Meetings began 3/31

## Upcoming Activities

- 10% Design rescheduled for 5/11/23

## Risks / Blocker / Activities Past Due

# Greensboro RPDC Transition Plan

	New Bid Cluster	Bid Cluster 1	Bid Cluster 2	Bid Cluster 3	Bid Cluster 4	Bid Cluster 5	Bid Cluster 6
<b>Current Bid Clusters</b>		Fayetteville NC P&DC	GREENSBORO NC P&DC	GREENSBORO NDC	RALEIGH NC P&DC	ROCKY MOUNT P&DF	ROANOKE VA P&DC
<b>Future Bid Clusters</b>							

Fayetteville P&DC	Bid Cluster	Finance #
FAYETTEVILLE NC P&DC	BC362680	362681
FAYETTEVILLE DOWNING RD ANNEX	BC362680	362692
FAYETTEVILLE NC PSA	BC362680	362694
FAYETTEVILLE NC VMF	BC362680	362682
FAYETTEVILLE PO	BC362680	362680
FAY-CLIFFDALE STA	BC362680	362683
FAY-TOKAY CARR ANX	BC362680	362684
FAY-LAKEDALE STA	BC362680	362685
FAY-HAYMOUNT STA	BC362680	362686
FAY-LAFAYETTE STA	BC362680	362687
FAY-EUTAW STA	BC362680	362689
FAY-FORT BRAGG BR	BC362680	362690
FAY - HIGHLAND ANNEX	BC362680	362693
LOG-FAYETTEVILLE NC PSA	BC362680	362677
LOG-FAYETTEVILLE NC P&DC	BC362680	362678
LOG-FAYETTEVILLE DOWNING RD ANNEX	BC362680	362679
MSSC - FAYETTEVILLE NC PO	BC362680	361003
WILMINGTON AUX VMF OF FAYETTEVILLE NC	BC362680	362691

Greensboro P&DC	Bid Cluster	Finance #
GREENSBORO NC P&DC	BC363192	363195
GREENSBORO NC VMF	BC363192	363196
GREENSBORO PO	BC363192	363192
GSO-WESTSIDE STA	BC363192	363201
GSO-HILLTOP CARRIER ANX	BC363192	363202
GSO-SPRING VALLEY STA	BC363192	363203
GSO-SUMMIT STA	BC363192	363204
GSO-MAIN OFFICE STA	BC363192	363205
LOG-GREENSBORO NC P&DC	BC363192	363189
MSSC - GREENSBORO NC PO	BC363192	361000
NORTH CAROLINA DISTRICT	BC363192	363197

Greensboro NDC	Bid Cluster	Finance #
GREENSBORO NC PSA	BC363193	363183
GREENSBORO NDC	BC363193	363193
LOG-GREENSBORO NC PSA	BC363193	363178
LOG-GREENSBORO NDC	BC363193	363188

RALEIGH NC P&DC	Bid Cluster	Finance #
LOG-RALEIGH NC MPA	BC366352	366341
LOG-RALEIGH NC P&DC	BC366352	366351
LOG-ROCKY MOUNT P&DF	BC366352	366611
MSSC - RALEIGH NC PO	BC366352	361001
RALEIGH NC MPA	BC366352	366343
RALEIGH NC P&DC	BC366352	366353
RALEIGH NC VMF	BC366352	366355
RALEIGH PO	BC366352	366352
RAL-CAPITOL STA	BC366352	366356
RAL-BRENTWOOD STA	BC366352	366357
RAL-AVENT FERRY STA	BC366352	366358
RAL-NORTH RIDGE STA	BC366352	366359
RAL-CAMERON VILLAGE STA	BC366352	366369
RAL-CREEKSIDE ANX	BC366352	366370
RAL-HILBURN STA	BC366352	366371
RAL-S RALEIGH CARRIER ANX	BC366352	366372
RAL-SUNNYBROOK STA	BC366352	366373

Rocky Mount PDF	Bid Cluster	Finance #
ROCKY MOUNT P&DF	BC366608	366610
ROCKY MOUNT PO	BC366608	366608
RKY-CARRIER ANX	BC366608	366609

Roanoke P&DC	Bid Cluster	Finance #
LOG-ROANOKE VA P&DC	BC517716	517701
LYNCHBURG AUX VMF OF ROANOKE VA	BC517716	517724
ROANOKE PO	BC517716	517716
ROA-CARRIER ANX	BC517716	517719
ROA-CAVE SPRING BR	BC517716	517720
ROA-GRANDIN ROAD STA	BC517716	517721
ROA-HOLLINS BR	BC517716	517722
ROA-MELROSE ST	BC517716	517723
ROANOKE VA P&DC	BC517716	517717
ROANOKE VA VMF	BC517716	517718
VIRGINIA DISTRICT	BC517716	517653

# **Santa Clarita Regional Processing & Distribution Center (RPDC)**

**Engineering Design**

**Logistics Design**

**Processing & Maintenance Transition,  
Implementation, & Complement**

# PPM/Engineering US-R-0005 Santa Clarita CA

This region covers northwestern Los Angeles County handling the following 3-digit ZIP codes:

932, 933, 935, 930, 931, 934, 910, 911, 912, 913, 914, 915, 916

The Regional Processing and Distribution Center is a repurposed USPS processing center building. If expanded USPS may be able to reuse legacy equipment. There are three associated Local Processing Centers in the region comprised of repurposed existing facilities.

The RPDC Region is centered in Santa Clarita, CA



# Santa Clarita RPDC Transition Plan



Timeline Update

# Santa Clarita CA – Processing Operations Transition/Implementation Status

Completed Activities

Upcoming Activities
<ul style="list-style-type: none"><li>• No Update</li></ul>

Risks / Blocker / Activities Past Due

# Santa Clarita RPDC Transition Plan

	New Bid Cluster	Bid Cluster 1	Bid Cluster 2	Bid Cluster 3	Bid Cluster 4
Current Bid Clusters		BAKERSFIELD CA P&DC	PASADENA CA MAIL PROCESSING ANNEX	SANTA BARBARA CA P&DC	SANTA CLARITA CA P&DC
Future Bid Clusters					

Bakersfield CA PDC	Bid Cluster	Finance #
BAKERSFIELD CA P&DC	BC050462	50464
BAKERSFIELD CA VMF	BC050462	50466
BAKERSFIELD PO	BC050462	50462
BAK-EAST BAKERSFIELD STA	BC050462	50463
BAK-BRUNDAGE STA	BC050462	50465
BAK-HILLCREST ANX	BC050462	50467
BAK-STOCKDALE ANX	BC050462	50468
BAK-SOUTH BAKERSFIELD STA	BC050462	50469
BAK-CAMINO MEDIA STA	BC050462	50470
BAK-OILDALE CARRIER ANX	BC050462	50471
BAK-DOWNTOWN STA	BC050462	50472
LOG-BAKERSFIELD CA P&DC	BC050462	50473
Pasadena MPA	Bid Cluster	Finance #
PASADENA CA MAIL PROCESSING ANNEX	BC055862	55870
PASADENA CA VMF	BC055862	58116
PASADENA PO	BC055862	55862
PAS-EAST PASADENA STA	BC055862	55864
PAS-SAN MARINO BR	BC055862	55865
PAS-JACKIE ROBINSON STA	BC055862	55866
PASADENA CFS	BC055862	55867
PAS-ORANGEWOOD STA	BC055862	55871
PAS-CATALINA STA	BC055862	55872
PAS-PLAZA STATION	BC055862	55873
VAN NUYS CA VMF	BC055862	58123

SANTA BARBARA CA P&DC	Bid Cluster	Finance #
LOG-SANTA BARBARA CA P&DC	BC056942	56961
OXNARD CA VMF	BC056942	56943
SANTA BARBARA CA P&DC	BC056942	56944
SANTA BARBARA PO	BC056942	56942
SBC-EAST BEACH CARRIER ANX	BC056942	56945
SBC-GOLETA BR	BC056942	56946
SBC-SAN ROQUE STA	BC056942	56947
SBC-ELLWOOD BR	BC056942	56970
SANTA CLARITA CA P&DC	Bid Cluster	Finance #
CALIFORNIA 3 DISTRICT	BC058100	58102
LOG-PASADENA CA MAIL PROCESSING ANNEX	BC058100	55869
LOG-VAN NUYS FSS MAIL PROCESSING ANX	BC058100	58125
LOG-SANTA CLARITA CA P&DC	BC058100	58141
MSSC - VAN NUYS CA PO	BC058100	51011
SANTA CLARITA CA P&DC	BC058100	58101
VAN NUYS FSS MAIL PROCESSING ANX	BC058100	58105
SANTA CLARITA CA VMF	BC058100	58104
VAN NUYS MAIN POST OFFICE	BC058100	58090
VAN NUYS PO	BC058100	58100
VAN-CVIC CENTER VAN NUYS STA	BC058100	58109
VAN-SHERMAN OAKS BR	BC058100	58111
VAN-ENCINO BR	BC058100	58114
VAN-PANORAMA CITY BR	BC058100	58115
VAN-BALBOA STA	BC058100	58131

# **Bethpage Regional Processing & Distribution Center (RPDC)**

**Engineering Design**

**Logistics Design**

**Processing & Maintenance Transition,  
Implementation, & Complement**

# US-R-0009 Bethpage NY

Plans for this region have changed and at this time  
Bethpage is no longer an active project

The region will be reevaluated at a later date
